ARCADIS Design & Consultancy for natural and built assets

Project Schedule
Regional Solid Waste and Recycling Master Plan
Solid Waste Disposal and Recyclable Materials
Processing Authority of Broward County, Florida

UPDATED: August 2, 2024 (3:30pm)

ID	Task Name	Duration	Baseline Start	Start	Start Variance	Baseline Finish	Finish	Finish Variance
1	**Regional Solid Waste and Recycling Master Plan**	**377 days**	**Fri 5/31/24**	**Fri 5/31/24**		**Sun 3/9/25**	**Wed 4/30/25**	**-52**
2	Client Service Planner	0 days	Fri 5/31/24	Fri 5/31/24	0	Fri 5/31/24	Fri 5/31/24	0
3	**Task 1 - Project Introduction and Kick-off Meeting**	**377 days**	**Fri 5/31/24**	**Fri 5/31/24**	**-14**	**Sun 3/9/25**	**Wed 4/30/25**	**-52**
4	Draft Project Framework Summary	54 days	Fri 5/31/24	Fri 5/31/24	0	Wed 7/17/24	Wed 7/17/24	0
5	Authority Review	5 days	Thu 7/18/24	Thu 7/18/24	0	Wed 7/24/24	Wed 7/24/24	0
6	Final Project Framework Summary	2 days	Thu 7/25/24	Thu 7/25/24	0	Fri 7/26/24	Fri 7/26/24	0
7	Data Request Memorandum	15 days	Fri 5/31/24	Fri 5/31/24	0	Thu 6/13/24	Thu 6/13/24	0
8	Data Received	41 days	Thu 6/13/24	Thu 6/13/24	0	Thu 6/20/24	Fri 8/9/24	-50
9	**Project Management Plan**	**377 days**	Fri 5/31/24	**Fri 5/31/24**	0	Sun 3/9/25	**Wed 4/30/25**	-52
10	Project Kick-Off Meeting	0 days	Fri 6/14/24	Fri 6/28/24	-14	Fri 6/14/24	Fri 6/28/24	-14
11	**Task 2 - Evaluate existing Solid Waste Disposal and Recycling Processes and Resources in Broward County**	**64 days**	**Thu 6/20/24**	**Fri 8/9/24**	**-50**	**Fri 8/16/24**	**Fri 10/4/24**	**-50**
12	Draft Existing Resources White Paper	50 days	Thu 6/20/24	Fri 8/9/24	-50	Sat 8/3/24	Sun 9/22/24	-50
13	Authority Review	5 days	Mon 8/5/24	Mon 9/23/24	-49	Fri 8/9/24	Fri 9/27/24	-49
14	Final Existing Resources White Paper	5 days	Mon 8/12/24	Mon 9/30/24	-49	Fri 8/16/24	Fri 10/4/24	-49
15	**Task 3 - Financial Overview**	**158 days**	**Thu 6/20/24**	**Fri 8/9/24**	**-50**	**Thu 11/7/24**	**Fri 12/27/24**	**-50**
16	Draft Financial Overview White Paper	60 days	Thu 6/20/24	Fri 8/9/24	-50	Mon 8/12/24	Tue 10/1/24	-50
17	Authority Review	5 days	Mon 8/12/24	Tue 10/1/24	-50	Mon 8/19/24	Tue 10/8/24	-50
18	Final Financial Overview White Paper	5 days	Thu 10/31/24	Fri 12/20/24	-50	Thu 11/7/24	Fri 12/27/24	-50
19	**Task 4 - Future Needs Assessment**	**61 days**	**Tue 7/2/24**	**Wed 8/21/24**	**-50**	**Fri 8/23/24**	**Mon 10/14/24**	**-52**
20	Draft Future Needs Assessment White Paper	45 days	Tue 7/2/24	Wed 8/21/24	-50	Sun 8/11/24	Mon 9/30/24	-50
21	Authority Review	5 days	Mon 8/12/24	Mon 9/30/24	-49	Fri 8/16/24	Mon 10/7/24	-52
22	Final Future Needs Assessment White Paper	5 days	Mon 8/19/24	Mon 10/7/24	-49	Fri 8/23/24	Mon 10/14/24	-52
23	**Task 5 - Regulatory Requirements and Policy Review**	**77 days**	**Thu 6/20/24**	**Fri 8/9/24**	**-50**	**Tue 8/27/24**	**Wed 10/16/24**	**-50**
24	Draft Regulatory Requirements and Policy Review White Paper	60 days	Thu 6/20/24	Fri 8/9/24	-50	Mon 8/12/24	Tue 10/1/24	-50
25	Authority Review	5 days	Mon 8/12/24	Tue 10/1/24	-50	Mon 8/19/24	Tue 10/8/24	-50
26	Final Regulatory Requirements and Policy Review White Paper	5 days	Wed 8/21/24	Wed 10/9/24	-49	Tue 8/27/24	Wed 10/16/24	-50
27	**Task 6 - Recommendations and Findings**	**46 days**	**Thu 9/26/24**	**Thu 11/14/24**	**-50**	**Tue 11/5/24**	**Wed 12/25/24**	**-50**
28	Draft Findings and Recommendations White Paper	30 days	Thu 9/26/24	Thu 11/14/24	-49	Tue 10/22/24	Wed 12/11/24	-50
29	Authority Review	5 days	Tue 10/22/24	Wed 12/11/24	-50	Tue 10/29/24	Wed 12/18/24	-50
30	Final Findings and Recommendations White Paper	5 days	Tue 10/29/24	Wed 12/18/24	-50	Tue 11/5/24	Wed 12/25/24	-50
31	**Task 7 - Implementation Plan and Timelines**	**41 days**	**Tue 10/22/24**	**Wed 12/11/24**	**-50**	**Wed 11/27/24**	**Thu 1/16/25**	**-50**
32	Draft Implementation Plan	25 days	Tue 10/22/24	Wed 12/11/24	-50	Wed 11/13/24	Thu 1/2/25	-50
33	Authority Review	5 days	Thu 11/14/24	Thu 1/2/25	-49	Wed 11/20/24	Thu 1/9/25	-50
34	Final Implementation Plan	5 days	Thu 11/21/24	Thu 1/9/25	-49	Wed 11/27/24	Thu 1/16/25	-50
35	**Task 8 - Education and Outreach**	**106 days**	**Thu 6/20/24**	**Fri 8/9/24**	**-50**	**Fri 9/20/24**	**Mon 11/11/24**	**-52**
36	Draft Education and Outreach Plan	90 days	Thu 6/20/24	Fri 8/9/24	-50	Sun 9/8/24	Mon 10/28/24	-50
37	Authority Review	5 days	Mon 9/9/24	Mon 10/28/24	-49	Fri 9/13/24	Mon 11/4/24	-52
38	Final Education and Outreach Plan	5 days	Mon 9/16/24	Mon 11/4/24	-49	Fri 9/20/24	Mon 11/11/24	-52
39	**Task 9 - Identify Innovative and Future Technologies**	**51 days**	**Mon 8/12/24**	**Mon 9/30/24**	**-49**	**Thu 9/26/24**	**Thu 11/14/24**	**-49**
40	Draft Technologies White Paper	35 days	Mon 8/12/24	Mon 9/30/24	-49	Thu 9/12/24	Thu 10/31/24	-49
41	Authority Review	5 days	Thu 9/12/24	Thu 10/31/24	-49	Thu 9/19/24	Thu 11/7/24	-49
42	Final Technologies White Paper	5 days	Thu 9/19/24	Thu 11/7/24	-49	Thu 9/26/24	Thu 11/14/24	-49
43	**Task 10 - Highlight Natural Areas Near Facilities**	**38 days**	**Tue 10/22/24**	**Wed 12/11/24**	**-50**	**Mon 11/25/24**	**Tue 1/14/25**	**-50**
44	Draft Natural Areas Educational Opportunities Report	22 days	Tue 10/22/24	Wed 12/11/24	-50	Mon 11/11/24	Tue 12/31/24	-50
45	Authority Review	5 days	Mon 11/11/24	Tue 12/31/24	-50	Mon 11/18/24	Tue 1/7/25	-50
46	Final Natural Areas Educational Opportunities Report	5 days	Mon 11/18/24	Tue 1/7/25	-50	Mon 11/25/24	Tue 1/14/25	-50
47	**Task 11 - Preparation of Draft Master Plan**	**8 days**	**Wed 11/27/24**	**Thu 1/16/25**	**-50**	**Wed 12/4/24**	**Thu 1/23/25**	**-50**
48	Draft Master Plan	0 days	Wed 11/27/24	Thu 1/16/25	-50	Wed 11/27/24	Thu 1/16/25	-50
49	Authority Review	5 days	Thu 11/28/24	Thu 1/16/25	-49	Wed 12/4/24	Thu 1/23/25	-50
50	**Task 12 - Conduct Workshops**	**240 days**	**Fri 7/26/24**	**Fri 7/26/24**	**-50**	**Fri 1/3/25**	**Mon 2/24/25**	**-52**
51	Draft 1st Workshop Presentation	32 days	Fri 7/26/24	Fri 7/26/24	0	Fri 8/23/24	Fri 8/23/24	0
52	Authority Review	5 days	Fri 8/23/24	Fri 8/23/24	0	Fri 8/30/24	Fri 8/30/24	0
53	Final 1st Workshop Presentation	14 days	Fri 8/30/24	Fri 8/30/24	0	Wed 9/11/24	Wed 9/11/24	0
54	Workshop 1	1 days	Wed 9/18/24	Wed 9/18/24	0	Wed 9/18/24	Wed 9/18/24	0
55	Draft 2, 3, 4, and 5 Workshop Presentation	21 days	Thu 11/28/24	Thu 1/16/25	-49	Mon 12/16/24	Tue 2/4/25	-50
56	Authority Review	5 days	Mon 12/16/24	Tue 2/4/25	-50	Mon 12/23/24	Tue 2/11/25	-50
57	Final 2, 3, 4, and 5 Workshop Presentation	7 days	Mon 12/23/24	Tue 2/11/25	-50	Sun 12/29/24	Mon 2/17/25	-50
58	Workshops 2, 3, 4, and 5	5 days	Mon 12/30/24	Mon 2/17/25	-49	Fri 1/3/25	Mon 2/24/25	-52
59	**Task 13 - Preparation of Final Master Plan**	**30 days**	**Sat 1/4/25**	**Mon 2/24/25**	**-51**	**Thu 1/30/25**	**Sun 3/23/25**	**-52**
60	Final Master Plan	30 days	Sat 1/4/25	Mon 2/24/25	-51	Thu 1/30/25	Sun 3/23/25	-52
61	**Task 14 - Develop Plan of Operations**	**43 days**	**Thu 1/30/25**	**Sun 3/23/25**	**-52**	**Sun 3/9/25**	**Wed 4/30/25**	**-52**
62	Draft Operations Plan	25 days	Thu 1/30/25	Sun 3/23/25	-52	Fri 2/21/25	Mon 4/14/25	-52
63	Authority Review	5 days	Fri 2/21/25	Mon 4/14/25	-52	Fri 2/28/25	Mon 4/21/25	-52
64	Final Operations Plan	10 days	Fri 2/28/25	Mon 4/21/25	-52	Sun 3/9/25	Wed 4/30/25	-52
65	**Task 15 - Facility Maintenance**	**43 days**	**Thu 1/30/25**	**Sun 3/23/25**	**-52**	**Sun 3/9/25**	**Wed 4/30/25**	**-52**
66	Draft Facility Maintenance Plan	25 days	Thu 1/30/25	Sun 3/23/25	-52	Fri 2/21/25	Mon 4/14/25	-52
67	Authority Review	5 days	Fri 2/21/25	Mon 4/14/25	-52	Fri 2/28/25	Mon 4/21/25	-52
68	Final Facility Maintenance Plan	10 days	Fri 2/28/25	Mon 4/21/25	-52	Sun 3/9/25	Wed 4/30/25	-52
69	**Task 16 - Project Management**	**377 days**	**Fri 5/31/24**	**Fri 5/31/24**	**0**	**Sun 3/9/25**	**Wed 4/30/25**	**-52**
70	Weekly Coordination Meetings with the Executive Director	377 days	Fri 5/31/24	Fri 5/31/24	0	Sun 3/9/25	Wed 4/30/25	-52

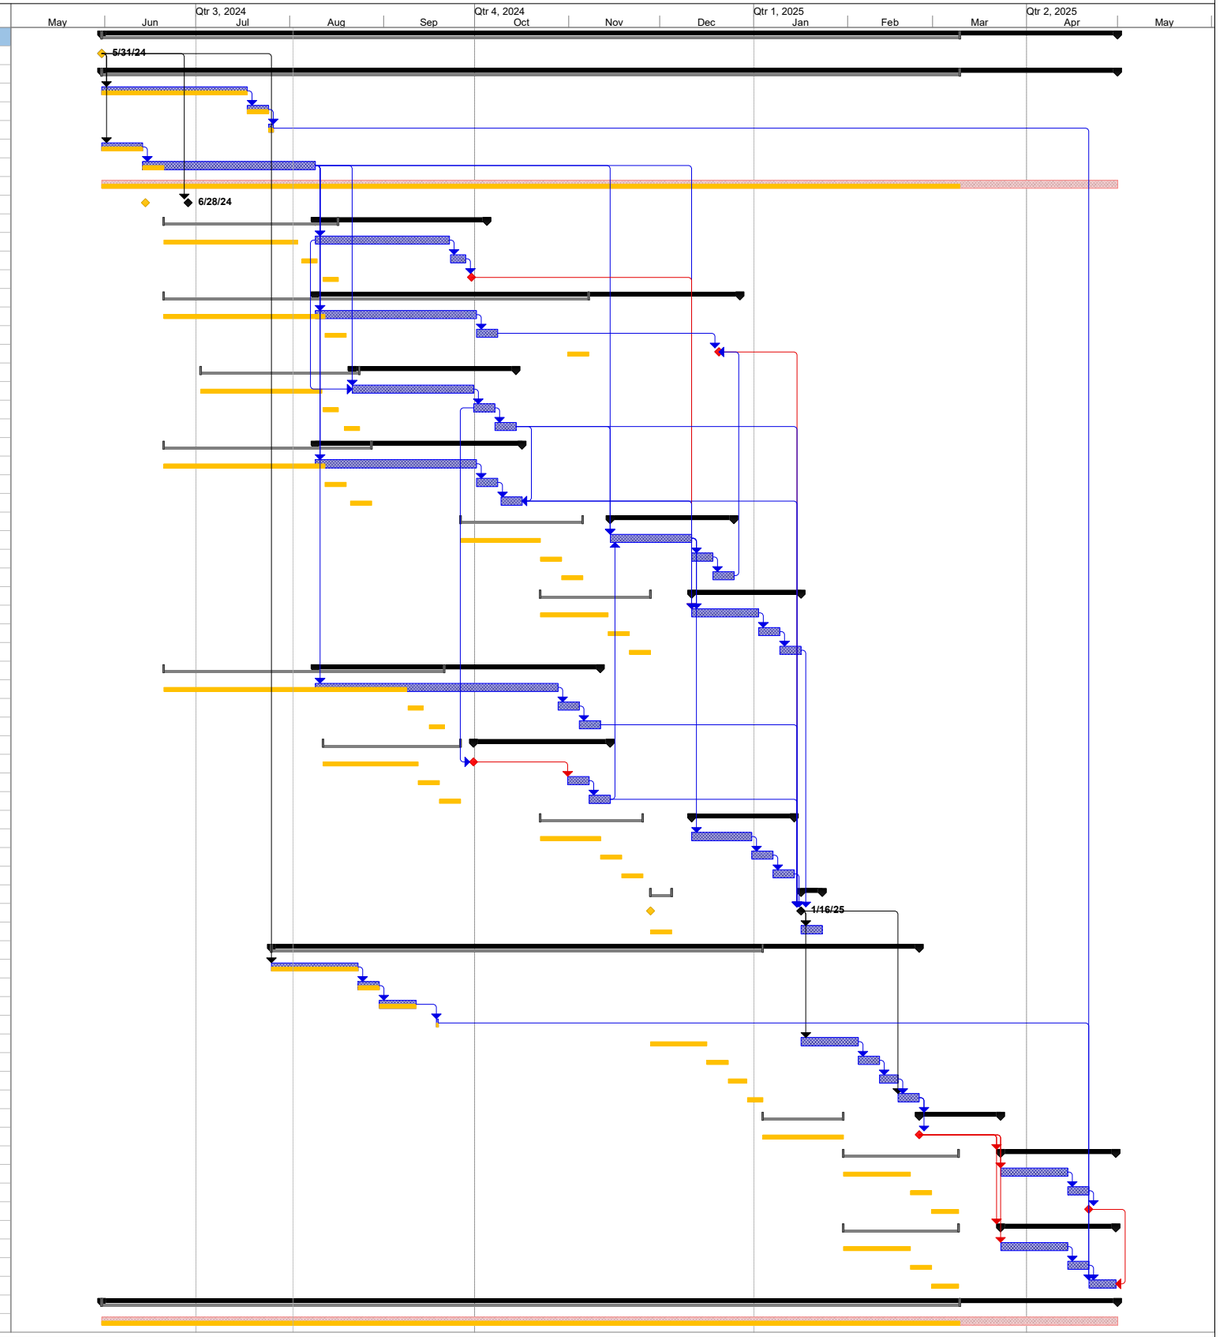

Project: Broward County Gant Chart 6
Date: March 24, 2009

Task · Milestone · Summary · Rolled Up Task · Rolled Up Milestone · Rolled Up Progress · Split · External Tasks · Project Summary · Group By Summary · Inactive Task · Inactive Milestone · Inactive Milestone · Inactive Summary · Manual Task · Duration-only · Manual Summary Rollup · Manual Summary · Start-only · Finish-only · External Tasks · External Milestone · Critical · Critical Split · Baseline · Baseline Milestone · Baseline Summary · Progress

SCS Engineers
